

Illinois State Water Survey
COOPERATING TECHNICAL PARTNERS (CTP)
FLOOD RISK PROJECT
MAPPING ACTIVITY STATEMENT (MAS)

MAS No. ISWS20-05 Lower Rock River HUC8 Continued Engagement

The Flood Risk Project described in this MAS dated June 2020 shall be completed in accordance with the CTP Partnership Agreement dated September 9, 2013 between Illinois State Water Survey (herein referred to as “CTP”) and the Federal Emergency Management Agency (FEMA).

DISCLAIMER (do not delete): In recognition of the MIP Studies Redesign which was deployed in June 2017, FEMA Region V has made an effort to update the accompanying “R5_MAS_SOW_Workbook” to align with terminology, projects, purchases and tasks in the redesigned MIP. The Region acknowledges that the signed SOW may or may not contain the required sections, tables, scope or terminology that is fully aligned with the FEMA Region V Workbook. Due to the reasons, the “R5_MAS_SOW_Workbook” will be treated as the sole source for creating and obligating projects, purchases and tasks in the redesigned MIP.

CONTENTS

SECTION 1—OBJECTIVE AND SCOPE	4
SECTION 3 – PERIOD OF PERFORMANCE.....	11
SECTION 4 – FUNDING/LEVERAGE (For CTP, OFA, and/or Community).....	11
SECTION 5 – STANDARDS.....	11
SECTION 6 – SCHEDULE.....	12
SECTION 7 – CERTIFICATIONS	12
SECTION 8 – TECHNICAL ASSISTANCE AND RESOURCES	13
SECTION 9 – CONTRACTORS	13
SECTION 10 – REPORTING	13
SECTION 11 – PROJECT COORDINATION	15
SECTION 12 – PROTECTION OF PRIVACY INFORMATION.....	16
SECTION 13 – POINTS OF CONTACT	17

SECTION 1—OBJECTIVE AND SCOPE

The objective of the Flood Risk Project documented in this Mapping Activity Statement is to develop and/or support flood hazard data and program-related tasks through completing technical risk analysis and mapping activities. These activities may or may not result in a new or updated Flood Insurance Rate Map (FIRM) and Flood Insurance Study (FIS) report for one or more communities within the project area.

A Rock River floodplain analysis was completed in 2014 as part of a previous Mapping Activity Statement contracted by FEMA for the purpose of updating the FIRMs in Henry, Rock Island and Whiteside Counties. Under MAS ISWS17-06 several tasks were funded to advance the project including re-engagement with communities, study of Meredosia Ditch, and development of models for streams within the foot print of planned PMRs. Minor revisions were made to the Rock River model and the study resubmitted to the Illinois Department of Natural Resources, Office of Water Resource (IDNR/OWR). IDNR/OWR has reviewed the updated model and issued a letter of concurrence dated April 17, 2020. All tasks under MAS ISWS17-06 are on schedule for completion, concluding with the task of a Flood Risk Review (FRR) planned for autumn 2020.

In the process of preparing work maps it was discovered the potential of flood waters from the Rock River extending west of Illinois Route 5/92 had not been given full consideration during the accreditation evaluation of levees that protect the City of East Moline from the Mississippi River and Sugar Creek. ISWS, FEMA and the RSC (STARR II) are, as of the preparation of this MAS, coordinating with the City of East Moline to evaluate any change in flood risk west of Illinois Route 5/92. It is agreed that the flood hazard analysis of the Rock River and subsequent mapping as submitted to IDNR/OWR for state concurrence, including the area up-stream or east of Illinois Route 5/92, will not change as it correctly represents the flood hazard if Illinois Route 5/92 acts as a hydraulically significant deterrent to flood waters. The only area in question for SFHA designation is east of Illinois Route 5/92 as shown in Figure 1 between Illinois Route 5/92 and the Mississippi River.

The objective of this MAS is for ISWS to continue to support FEMA's and the RSC's engagement with the City of East Moline and to integrate into work maps the resulting flood hazard mapping west of Illinois Route 5/92 through the city of East Moline to the Mississippi River to be prepared by the RSC. This MAS does not include any revisions to the Rock River engineering study or mapping. A FRR meeting is funded under MAS ISWS17-06 and the updated work maps will be presented at the FRR meeting tentatively planned for autumn 2020.

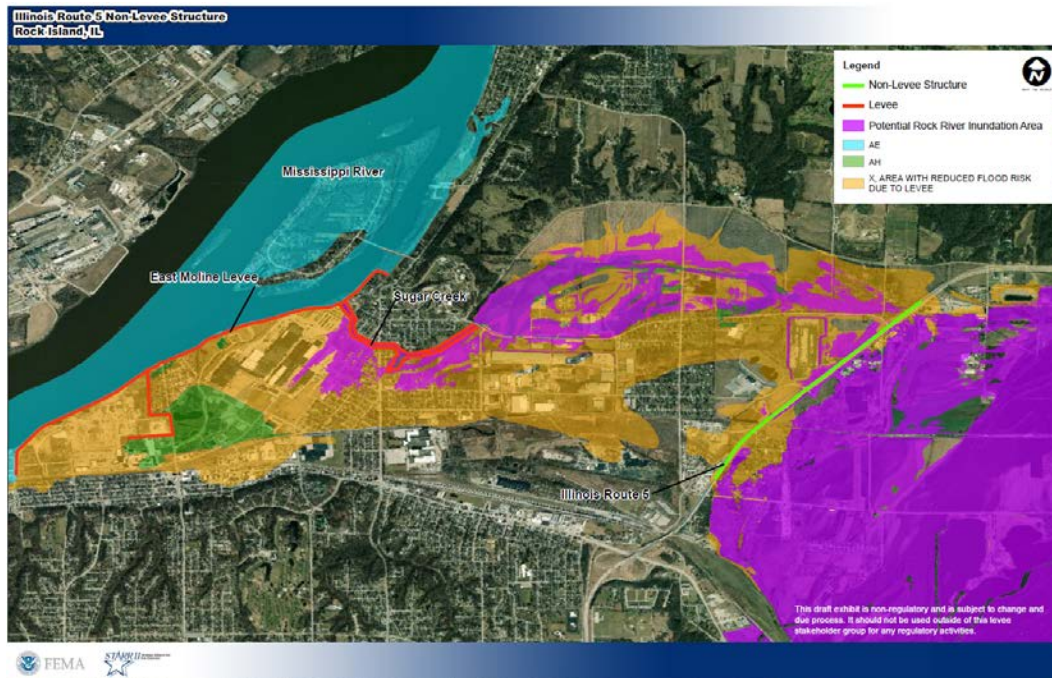


Figure 1. Possible flood mapping scenario west of Illinois Route 5/92

The watersheds and jurisdictions in which Flood Risk Projects will be performed, as well as their applicable project type/activities, are summarized in Table 1.1: Flood Risk Project Watersheds and Jurisdictions. All applicable project activities should be identified in the last column of the table for each watershed, county/parish or community listed in Table 1.1 (e.g., Discovery only, Discovery and Flood Risk Products, FIRM/FIS updates, Prelim Distribution, Post-Preliminary Processing). Watershed Reports will be created and distributed to counties/parishes and communities identified as including Discovery in the Project Type. Table 1.1: Flood Risk Project Watersheds and Jurisdictions

Watershed	Geographic Footprint	Counties/Parishes and Communities Included in Project	Project Type
Lower Rock River Watershed	Rock River Floodplain in Henry, Whiteside and Rock Island Counties	- Whiteside County - City of Rock Falls - City of Sterling - Village of Lyndon - Village of Prophetstown - Village of Erie - Rock Island County - City of Moline - Village of Hillsdale - City of East Moline - City of Silvis	Community Engagement and Project Outreach for Rock River floodplain analysis

Watershed	Geographic Footprint	Counties/Parishes and Communities Included in Project	Project Type
		▪ Village of Coal Valley ▪ Village of Milan ▪ City of Rock Island ▪ Henry County ▪ City of Colona ▪ Village of Cleveland	

This Flood Risk Project will be completed by the following entities:

- Illinois State Water Survey.

The CTP shall notify FEMA and all applicable parties of all meetings with community officials, and other relevant meetings, between three and six weeks prior to the meeting (with as much notice as possible). FEMA and/or its contractor may or may not attend the community meetings.

The CTP shall maintain an archive of all data submitted. All supporting data must be retained for three years from the date a funding recipient submits its final expenditure report to FEMA. The CTP must demonstrate to FEMA compliance with Subpart 24.1 of the Federal Acquisition Regulation (FAR) related to the handling of Personally Identifiable Information (PII) associated with the Activities listed in this MAS.

The CTP is responsible for providing a Quality Management Plan (QMP) to include an independent Quality Assurance/Quality Control (QA/QC) plan for all assigned activities. The CTP will submit a Summary Report that describes and provides the results of all automated or manual QA/QC review steps. The report should include the process for all assigned activities. The QMP is delivered directly to the FEMA Regions.

Independent QC review activities may be performed by the CTP or FEMA's contractor at the discretion of FEMA. If the CTP will be responsible for the QC review, the entity that will perform QC should be identified in this MAS. The CTP will need to submit its QC plan to the Regional Project Officer for approval.

Please note FEMA will also be performing periodic audits and overall study/project management to promote quality, including National Quality Reviews (QR) required per FEMA standards for all Flood Risk Projects. Whether or not the CTP performs the Independent QC review mentioned in the preceding paragraph, the CTP will be responsible for addressing any and all comments resulting from National QRs and any additional independent QA reviews required by the FEMA Regional Office, including re-submittal of deliverables as needed to pass technical or quality review. The CTP will submit regulatory products to FEMA's designated National QR reviewer (for QR 1-8 reviews) for review and approval prior to public issuance.

Metadata is required for certain activities. The FEMA current, applicable metadata guidelines will be followed.

FIRM-related tasks require a passing QC Report from FEMA's National FIRM database auto-validation tool, the Database Validation Tool (DVT) for QRs #1, #2, and #5 as required in FEMA standards. DVT can be found in the Mapping Information Platform tasks that correspond to the QRs: Draft FIRM Database Capture, Produce Preliminary Products Data Capture, and Final Mapping Products Data Capture. Training materials for this step are available on the Mapping Information Platform (MIP) at MIP User Care Training Materials.

FEMA will provide download/upload capability for data submittals through the MIP located at <https://hazards.fema.gov>. As each activity is completed, the data must be submitted to the MIP by the CTP or other designee. After data is submitted, a Validation task must be completed. Note that FEMA's designee will be assigned this task, not the CTP

The CTP assigned to the activity will respond to any comments generated as a result of the mandatory quality control checks by the Production and Technical Services (PTS) contractor. The PTS QC process is nationally funded and required on each non-PTS study.

In cooperation with the FEMA Project Officer, a Project Management Team (PMT) will be established by the CTP consisting of representatives from the CTP, FEMA's Regional Engineer, and other appropriate parties (e.g., FEMA contractors) at the discretion of FEMA. The PMT will be responsible for coordinating the activities identified in this MAS. The FEMA Region will be provided with documentation identifying the established PMT. The PMT will include representatives from the Illinois Department of Natural Resources/ Office of Water Resources, the FEMA Region 5 Engineer assigned to Illinois, the RSC (STARR II), and the Illinois State Water Survey (ISWS), Coordinated Hazard Assessment Mapping Program Section Head or their designee.

Responsible Mapping Partner: ISWS

Scope: Project Management is the active process of planning, organizing, and managing resources toward the successful accomplishment of predefined project goals and objectives. The CTP will coordinate with the FEMA Regional Office with respect to Project Management activities and technical mapping activities.

Earned Value Data Entry

The FEMA Mapping Information Platform (MIP) is designed to track the earned value of Flood Risk Projects. This information is automatically calculated by the MIP, using the actual cost and schedule of work performed, or "actuals," and comparing them to the expected cost and schedule of work performed, or "baseline."

Once the FEMA Regional Office has funded a project, FEMA or its contractor will create the tasks in the MIP. This step establishes the baseline for the project in the MIP, using the cost and schedule information for each task as outlined in this document.

The MIP study application allows FEMA and the CTP to manage the status of these projects at a task level. The cost and schedule information, updated monthly by the CTP for each contracted task, is

compared to the baseline established for those tasks. This information is rolled up to a project level and monitored by the FEMA Region to assess progress and earned value.

Earned Value data entry involves updating cost, schedule, and performance (physical percent complete), and as of date in the MIP by the CTP each month for each assigned task.

Once the baseline has been established in the MIP, the CTP shall input the performance and actual cost to date for all tasks within each project for which the CTP is responsible. This must be completed at a minimum once every 30 days and at the completion of the task. When a task is completed and has been validated (if applicable), the CTP shall enter 100 percent complete, enter the actual completion cost, and the actual completion date within the Track Task Progress Workbench as applicable. The tasks will be available on the Track Progress workbench up to 90 days after the completion of the producer task in each purchase.

The MIP shall also be populated with appropriate leverage information regarding who (CTP or community) paid for the data provided and the amount of data used by the Flood Risk Project. The CTP will maintain a Schedule Performance Index (SPI) and Cost Performance Index (CPI) between 0.92 and 1.08. Special Problem Reports (SPR) explaining any variance must be submitted in a timely manner as required.

The CTP is required to report on the earned value of projects that are in the MIP monthly and must give explanations for variances outside of the tolerance defined above. FEMA Regional Offices must implement a Corrective Action Plan (CAP) when a CTP partner is outside of the tolerance. A CAP must define the reason for the variance and the intended resolution. FEMA Regional Offices must coordinate with FEMA Headquarters when CAPs are developed.

Program Management and overarching Community Outreach and Mitigation Strategies (COMS) SOW tasks are now tracked in the MIP. Cost and schedule performance measures must be defined and documented in those separate MAS or SOW. These measures must be used to monitor partner performance and to determine future funding eligibility. This exception only applies to tasks not able to be conducted or tracked in the MIP.

The Project Officer, as needed, may request additional information on status of the project on an ad hoc basis.

Standards: All PM work shall be performed in accordance with the standards specified in Section 5 – Standards.

Deliverables: The CTP shall deliver the following checked item(s) to the FEMA Regional Project Officer (please click/check the box of the deliverables included in this MAS):

☒	Monthly earned value data reporting through the MIP with variance explanations to support management of technical mapping activities within specified time frame, for both Regulatory and Flood Risk Products
☐	Management of SPI/CPI performance for an organization
☐	Overall project Quality Management Plan including QA/QC maintenance information, such as maintaining a QA/QC log and providing a QA/QC approach to FEMA for review and approval
☐	Management of adherence to scope of work and quality of work for an organization
☐	Other: {Insert additional details} .

Project Risk Identification and Mitigation

Responsible Mapping Partner: ISWS.

Risks to the planned completion of a project may come from various sources. Risks should be identified during the planning phase and monitored throughout the project, so that potential impact can be assessed, and solution strategies developed and implemented as needed.

Table 1.3: Project Risk Identification

Project Risk	Potential Impact	Solution Strategy
Inability for FEMA and the City of East Moline to reach agreement for floodplain mapping west of Illinois Route 5/92 by autumn of 2020	Draft work map preparation delayed, delay of Flood Risk Review meeting which impacts overall project.	Show disputed area as last modeled by STARR II or show area as TBD on work maps used at FRR meeting.
Community engagement extends beyond Fall of 2020 exceeding the time allocated by ISWS for coordination.	Cost overrun or ISWS lack of involvement and support for FEMA and RSC	Carefully manage time. ISWS will closely monitor time spent for engagement and keep FEMA and RSC informed.
Community produces technical data that demonstrates impact to floodplain mapping east of Illinois Route 5/92.	While highly unlikely, should such data and analyses be technically sound the Rock River model would have to be revised causing extreme delays and requiring substantial funding to complete project.	Work closely with community and quickly evaluate any new technical data provided and the potential impact on the model and/or delineation of the Rock River flood risk.
Community pursues extension of the currently accredited levee system on Sugar Creek or other physical improvements with the intent to modify potential floodplain delineation.	Planning, design, permitting, construction, certification, and accreditation process for potential improvements may be concurrent with FEMA mapping phase activities within Rock Island, Henry and Whiteside Counties. Accreditation status may result in delay, comments or appeal.	Continued coordination toward resolution of this project risk is not included in the MAS No. ISWS 20-05. Potential increased cost and/or project duration for the mapping or other Rock River watershed phases should be considered for future funding years.

Project Outreach and Communication Plan (POCP)

The CTP will work with the FEMA Regional Office during the initiation of this activity to develop the Project Outreach and Communication Plan (POCP) to support the implementation of the mapping project. The FEMA Regional Office will have access to many customizable outreach tools that have been developed for this process to support each touchpoint that the PMT has with the community.

Standards: All Community Engagement and Outreach work shall be performed in accordance with the standards specified in Section 5 – Standards. All communication with local governments will be done in accordance with 44 CFR Part 66.

Deliverables: The CTP shall deliver the following checked items to the FEMA Regional Project Officer in accordance with the schedule outlined in Section 6 – Schedule and include within the Technical Support Data Notebook (TSDN):

☒	A Project Communication Plan detailing outreach and coordination activities. NOTE: The MIP has tasks available to capture Outreach activities. Upon completion of these tasks, please upload relevant data to those tasks in the MIP. ¹
☐	Watershed/Community Assessment outputs, including logs of telephone discussions (if applicable)
☐	Meeting invitation, agenda, presentation slides (as requested), and meeting notes for FEMA review
☐	Action Identification and Advancement Plan (if applicable)
☐	Project update status reports for project communities
☐	Provide documentation of adherence with the requirements for the community 30-day review of proposed models and 30-day review of work maps, completed models, and associated information

SECTION 2 – TECHNICAL AND ADMINISTRATIVE SUPPORT DATA SUBMITTAL

The Project Team members for this Flood Risk Project that have responsibilities for activities included in this MAS shall comply with the data submittal requirements summarized below and in appropriate guidance.

All supporting documentation for the activities in this MAS shall be submitted according to FEMA standards and requirements and will include a FEDD folder. Submittals must be made to the appropriate PTS for a review of required materials. The CTP will respond to requests from FEMA or its contractors for additional information and ensure that all required documents are included in the TSDN.

If any issues arise that could affect the completion of an activity within the proposed scope or budget, the CTP shall complete and submit to FEMA a Special Problem Report (SPR) as soon as possible after the issue is identified. The SPR describes the issue and proposes possible resolutions. For additional information on SPRs, consult the FEMA Regional Office.

¹ All products should be uploaded to the MIP (or submitted to MIP Help on a hard drive if they are over the size listed in the MIP Guidance document)

Information supporting FEMA standards and requirements regarding the TSDN and FEDD file may be found in the “Technical Reference: Data Capture” document and other associated guidance documents.

SECTION 3 – PERIOD OF PERFORMANCE

The mapping activities outlined in this MAS will be completed as specified in the Cooperative Agreement Funding Opportunity Announcement, Award Notice and/or Articles of Agreement. The Mapping Activities may be terminated at the option of FEMA or the CTP in accordance with the provisions of the Partnership Agreement dated **September 9, 2013**. If these mapping activities are terminated, all products produced to date must be submitted and updated into the MIP (if applicable) and the remaining funds, provided by FEMA for this MAS, from uncompleted activities will be returned to FEMA.

SECTION 4 – FUNDING/LEVERAGE (For CTP, OFA, and/or Community)

FEMA is providing funding, in the amount of **\$60,400** through a Cooperative Agreement to **Illinois State Water Survey** for the completion of this Flood Risk Project. During the discovery process, additional needs may be identified. Activities associated with any additional needs would be performed based on availability of additional funds. See Table 4.1.

Table 4.1: Contribution and Leverage

TASK, PARTNER, COST and SCHEDULE					
Project Task	FEMA Contribution	Partner Contribution (CTP Only)	Breakout Cost (if applicable)	% Partner (CTP Only) Leverage (of Total Project Task Cost)	Total Project Task Cost (FEMA + Partner)
Miscellaneous Tasks					
Project Management	\$11,049.00	\$0.00	NA	%	\$11,049.00
Project Risk ID & Mitigation	\$32,901.00	\$0.00	NA	%	\$32,901.00
Perform Community Engagement & Project Outreach	\$16,450.00	\$0.00	NA	%	\$16,450.00
	\$60,400.00	\$0.00	\$0.00	0%	\$60,400.00

SECTION 5 – STANDARDS

The standards relevant to this MAS are presented in FEMA Policy 204-078-1 Standards for Flood Risk Analysis and Mapping, Revision 10, dated November 2019, located at <http://www.fema.gov/media-library/assets/documents/35313>. This Policy supersedes all previous standards included in the *Guidelines and Specifications for Flood Hazard Mapping Partners*, including all related appendices and Procedure Memorandums (PMs). Additional information and links to FEMA Technical References, guidance documents, templates and other resources may be accessed and downloaded at <http://www.fema.gov/guidelines-and-standards-flood-risk-analysis-and-mapping>. Revisions to the Policy memo are made on a regular basis. Some changes / updates are considered low impact, not requiring any scope, financial, process or technology changes to implement. CTPs should always check for the latest version of the policy memo to evaluate potential standards updates.

To facilitate the use of standards and related documents, users can access the FEMA *Guidelines and Standards Master Index* located here: www.fema.gov/media-library/assets/documents/94095. This index provides a cross-reference of documentation available for Flood Risk Projects, Letters of Map Change and related Risk MAP activities. The cross-referenced relationships are organized and accessible through linkages for standards, guidance, technical references and templates. The master index is updated in coordination with the FEMA Policy Memo noted above.

CTPs and their sub-awardees must comply with FEMA’s Federal Regulations in Chapter 44 of the Code of Federal Regulations (CFR), specifically CFR Parts 65, 66 and 67, and the appropriate year CTP Notice of Funding Opportunity and Agreement Articles. CTPs shall also coordinate with their Regional office to determine additional standards that should be met.

SECTION 6 – SCHEDULE

To accurately document Risk MAP activities, there are two tools available for identifying mapping activities as they align to the Mapping Information Platform (MIP). The activities documented in this MAS shall be completed in accordance with either Table 6.1 Project Activities Schedule or the Mapping Information Platform (MIP) MAS/SOW Workbook.²

Please work with your FEMA Region when submitting the MIP MAS/SOW Workbook or any other form that is representative of the information in Table 6.1. Table 6.1, the MIP MAS/SOW Workbook or a similar table is required and needs to be filled out and documented in this MAS as part of the grant’s submission process.

Table 6.1: Project Activities Schedule

<i>Project Task</i>	<i>Baseline Start Date</i>	<i>Baseline End Date</i>
Miscellaneous Tasks		
Project Management	09/15/2020	9/15/2021
Project Risk ID & Mitigation	09/15/2020	9/15/2021
Perform Community Engagement & Project Outreach	09/15/2020	9/15/2021

See R5_MAS_SOW worksheet tab “20-05_Lower_Rock”

The CTP will coordinate with FEMA, or its designee, to develop a baseline schedule for individual project activities. FEMA or its designee will utilize the individual project task schedule create the Flood Risk Project in the MIP and baseline the project activities with schedule and cost information within 30 days of the funds being awarded and FEMA’s approval of the final cost and schedule. The baseline schedule for individual project activities may be re-baselined in the MIP with approval from the FEMA Project Officer, and does not require a change to this MAS unless the overall project end date is modified.

SECTION 7 – CERTIFICATIONS

Data Capture

² You must sign into the CTP Collaboration Center to access this form. If you are not a registered user, please visit: <https://www.surveymonkey.com/r/CTPCollaborationCenterRegistration>

- **Data Capture:** Please refer to the current “Technical Reference: Data Capture” document, located at <https://www.fema.gov/media-library/assets/documents/34519>, for instructions on certifications. Generally, each Data Capture task includes certification forms and a project narrative. Mapping Partners should complete and submit only one Certification of Completeness and/or one Certification of Compliance form when the task is complete.

SECTION 8 – TECHNICAL ASSISTANCE AND RESOURCES

Project Team members may obtain copies of FEMA-issued LOMCs, archived engineering backup data, and data collected as part of the CNMS process from FEMA and/or your Regional Project Officer.

General technical and programmatic information can be downloaded from the FEMA website at <https://www.fema.gov/cooperating-technical-partners-program>. Specific technical and programmatic support may be provided through FEMA and/or its contractor; such assistance should be requested through the FEMA Project Officer specified in Section 12 – Points of Contact.

Project Team members also may consult with the FEMA Regional Project Officer to request support in the areas of selection of data sources, digital data accuracy standards, assessment of vertical data accuracy, data collection methods or subcontractors, and GIS-based engineering and modeling training. Please contact the region to obtain the most recent version of the Risk MAP timeline.

Assistance with the MIP may be requested at miphelp@RiskMAPcds.com.

SECTION 9 – CONTRACTORS

The CTP does not intend to use the services of a contractor for this SOW. No transfer of funds to agencies other than those identified in the approved cooperative agreement application shall be made without prior approval from FEMA. The CTP shall ensure that the procurement for all contractors, if any are used for this SOW, complies with the requirements of 2 CFR Part 200.

Guidance provided in this part includes, but is not limited to, contract administration and recordkeeping, notification requirements, review procedures, competition, methods of procurement, and cost and pricing analysis. The 2 CFR 200 documents may be viewed online at <http://www.ecfr.gov/cgi-bin/text-idx?SID=cc011f4fb962e68cb0da4bc91e8fbb43&mc=true&node=pt2.1.200&rgn=div5>. Additionally, contractors must not pose a conflict of interest issue.

SECTION 10 – REPORTING

Financial Reporting: Because funding has been provided to the CTP by FEMA, financial reporting requirements for the CTP will be in accordance with the terms of the Cooperative Agreement Funding Opportunity Announcement, Articles of Agreement or Award Notice for this MAS. The CTP shall also refer to 2 CFR Part 200.. ISWS through the University of Illinois shall provide financial reports to the FEMA Regional Project Officer and Assistance Officer in accordance with the terms of the signed Cooperative Agreement for this MAS.

Performance Reporting: Recipients are responsible for providing a signed performance report using the required list of information shown in the NOFO (or and old SF-PPR if you prefer) on a quarterly basis throughout the period of performance, including partial calendar quarters as well as for periods where no grant award activity occurs. The CTP shall refer to 2 CFR Part 200 to obtain minimum requirements for progress reporting. The Project Officer, as needed, may request additional information on progress.

The CTP may meet with FEMA and/or its contractor(s) as frequently as needed to review the progress of the project in addition to the quarterly financial and status submittals. These meetings may alternate between FEMA's Regional Office, the ISWS office, and conference calls, as necessary.

The CTP must report performance of the grant in conjunction with the progress reporting. The performance of the CTP is measured by the following criteria. Quantitative Targets for performance measures will be defined using the *FY2020 DHS NOFO for CTPs Appendix D Performance Measure References*, "*CTP Performance Measures Matrix*" in conjunction with your FEMA PM and defined in Table 10.1.

Table 10.1: Performance Measures Targets

See CTP_Metrics_2020. xlsx for Summary of ISWS Performance Measures Targets

Output Measurement Options	Recorded Metric Unit/Scale	Lower Rock River HUC8 Continued Engagement
		ISWS20-05
0.92 to 1.08	SPI score (EV/planned value) CPI score (EV/actual cost)	0.92 to 1.08
1. Grant amendments that are not outside the CTPs span of control will be evaluated and documented. 2. Excessive CRs that are due to project management issues within the CTP's control will require additional discussion and possible development of a quality performance plan to identify a continued path to improved project and program management. 3. Reporting within specified timelines throughout the project.	# of CRs 0=no CRs 1=amendment needed outside of control 2=amendment needed within control 3=multiple amendments needed within control	Goal: 0
Monthly updates for all cases, including (%) of active tasks per	Achieved / Not achieved	Monthly MIP update
2. Ongoing and regular coordination with other state/local offices to discuss agency's prioritization process for Risk MAP projects as well as schedules, meetings, strategy development and stakeholder engagement.	Achieved / Not achieved	Monthly calls with FEMA & IDNR/OWR

The CTP shall communicate with communities throughout the life of each project. Continued engagement is necessary and appropriate and will build upon the relationships established or enhanced during Discovery and provide transparency into the Risk MAP process. This may occur through monthly or quarterly updates or project status calls with community leaders, project websites including updates at several milestones or along a specific timeline, or other methods.

SECTION 11 – PROJECT COORDINATION

Throughout the project, all members of the Project Team will coordinate, as necessary, to ensure the products meet the technical and format specifications required and contain accurate, up-to-date information. Coordination activities may include:

- Meetings, teleconferences, and/or video conferences with FEMA and other Project Team members **will be conducted as per the communication plan.**
- Telephone conversations with FEMA and other Project Team members on a **monthly** basis, and an ad hoc basis, as required.
- Updates to the MIP and other FEMA status information systems in accordance with FEMA standards and requirements.
- E-mail, facsimile transmissions, and letters, as required.

SECTION 12 – PROTECTION OF PRIVACY INFORMATION

To accomplish the tasks outlined in this scope, FEMA will provide the CTP access to Risk Analysis Management (RAM) which includes all PII collected in RAM as outlined in DHS/FEMA/PIA-045 Hazard Mitigation Planning and Flood Mapping Products and Services Support Systems.

<https://www.dhs.gov/publication/dhsfemapia-045-hazard-mitigation-planning-and-flood-mapping-products-and-services>

The information sharing outlined in this scope authorized by the following System of Records Notice(s) and Routine Use(s): DHS/FEMA-014 Hazard Mitigation Planning and Flood Mapping Products and Services Records System of Records. <https://www.federalregister.gov/documents/2017/10/25/2017-23205/privacy-act-of-1974-system-of-records>

When necessary to accomplish a function related to this system of records, CTPs (term used to include any subrecipients and/or contractors used by the CTP for this work) must comply with the Privacy Act. Individuals provided information under this routine use are subject to the same Privacy Act requirements and limitations on disclosure as are applicable to DHS officers and employees.

The mapping program for the NFIP, implemented through Risk MAP, is established through the National Flood Insurance Act of 1968, as amended and the Biggert-Waters Flood Insurance Reform Act of 2012 (BW-12), as amended (42 U.S.C. 4001 et seq.). The mapping program is governed by the implementing regulations at Code of Federal Regulations - Title 44 (44 CFR) parts 59-72.

The CTP will limit access to the PII provided by FEMA under this contract only to the CTP's authorized personnel who need to know the information to accomplish the tasks outlined in this contract.

Definition. As used in this section, "personally identifiable information" means information that can be used to distinguish or trace an individual's identity, either alone or when combined with other information that is linked or linkable to a specific individual. (See Office of Management and Budget (OMB) Circular A-130, Managing Federal Information as a Strategic Resource).

- A. The CTP will ensure that initial privacy training, and annual privacy training, thereafter, is completed by CTP employees, subrecipients and/or contractors and subcontractors who
 - i. Have access to a system of records.
 - ii. Create, collect, use, process, store, maintain, disseminate, disclose, dispose, or otherwise handle personally identifiable information on behalf of an agency; or
 - iii. Design, develop, maintain, or operate a system of records
- B. FEMA will provide the link to external facing initial privacy training, and annual privacy training thereafter, to CTPs for the duration of this grant.
- C. The CTP shall maintain and, upon request, provide documentation of completion of privacy training to FEMA.
- D. The CTP shall not allow any employee access to a system of records, or permit any employee to create, collect, use, process, store, maintain, disseminate, disclose, dispose or otherwise handle personally identifiable information, or to design, develop, maintain, or operate a system of records unless the employee has completed privacy training, as required by this section.

The CTP will ensure no computer matching, as that term is defined in U.S.C. § 552a(o), will occur for the purpose of establishing or verifying eligibility or compliance as it relates to cash or in-kind assistance of payments under federal benefit programs.

If at any time during the term of this cooperative agreement any part of FEMA PII, in any form, that the CTP obtains from FEMA ceases to be required by the CTP for the performance of the scope, or upon termination of the cooperative agreement, whichever occurs first, the CTP shall, within fourteen (14) days thereafter, promptly notify FEMA and securely return PII to FEMA, or, at FEMA's written request destroy, un-install and/or remove all copies of such PII in the CTP's possession or control, and certify in writing to FEMA that such tasks have been completed.

SECTION 13 – POINTS OF CONTACT

The points of contact for this Flood Risk Project are **John Wethington**, the FEMA Regional Project Officer; **Sally McConkey**, the Project Manager for **ISWS**; or subsequent personnel of comparable experience who are appointed to fulfill these responsibilities. When necessary, any additional FEMA assistance should be requested through the FEMA Regional Project Officer.

Each party has caused this MAS to be executed by its duly authorized representative.



08/10/2020

Sally McConkey
Project Manager

Date

John Wethington
Regional Project Officer
Federal Emergency Management Agency, Region 5

Date

Julia McCarthy
Risk Analysis Branch Chief
Federal Emergency Management Agency, Region 5

Date

Mary Beth Caruso
Mitigation Division Director
Federal Emergency Management Agency, Region 5

Date
